



**SAN JOAQUIN**  
— COUNTY —  
*Greatness grows here.*




# San Joaquin County Advisory Water Committee

## Stream and Precipitation Gage Project Update

April 15, 2026

## San Joaquin County Stream and Precipitation Gage Network Update

- Grants Received
  - CalSIP – California Stream Gage Improvement Program
    - \$148,000
  - Delta Round 2 – Delta Flood Emergency Response Grant Round 2
    - \$273,000 - \$58,500 is for new gages
  - Statewide Round 3 – Statewide Flood Emergency Response Grant Round 3
    - \$583,950 - \$80,000 is for new gages
  - OES Grant
    - \$200,000

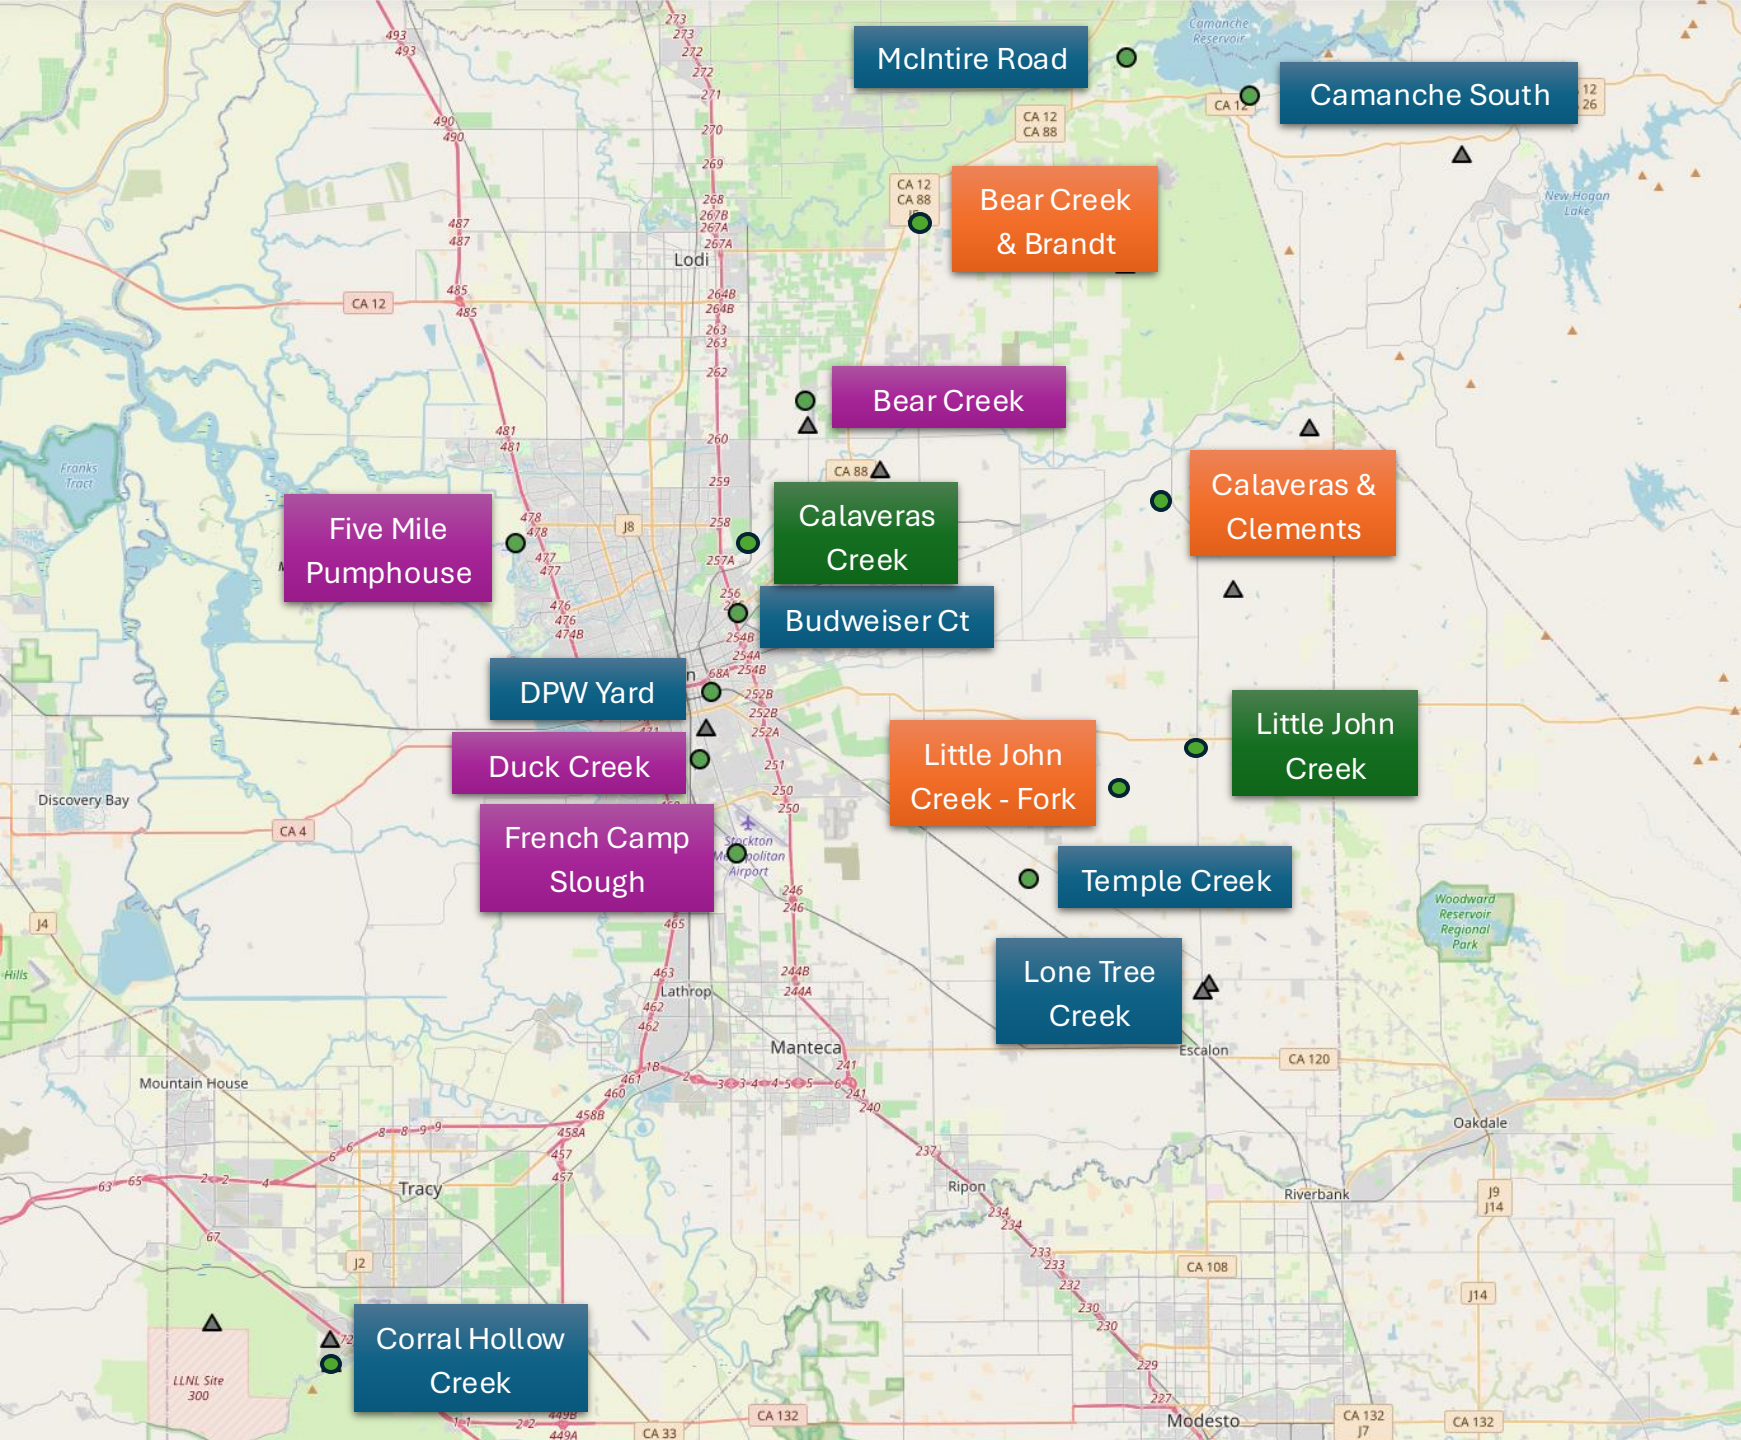

# SJC Stream Gage Network

- CalSIP
  - Upgrade 4 existing gages with new components and flow sensors
  - Anticipated completion in September 2026
- Delta 2 Gages
  - Installed 2 new gages
  - Gages are installed
- Statewide 3
  - Will install 3 new gages
  - Anticipated completion in August 2026
- OES DWR 3 Grant
  - Working to find locations
  - Will be in Delta area
- Existing Stream Gages
  - Will upgrade similar to CalSIP

# Questions
